To,
The Maharera,

10-01-2024


Dear Sir,

Subject: Submission of Bar Chart for progress in execution of balance construction of Project Name :Vista 3C RERA No: P50500007884

As per point D of the final order of the extension given to Luxora Infrastructure Pvt. Ltd. in Regulatory case No 89 of 2023, we have enclosed the following documents for your perusal:

1. Bar Chart indication achieved construction versus proposed construction schedule


We will be providing monthly updates on the progress of construction.



Promoter

Luxora Infrastructure Pvt. Ltd.
CIN: U70100MH2007PTC166943,
150 Avior Corporate Park, Nirmal Galaxy,
LBS Road, Mulund, Mumbai-400080
Ph: +91 22 25908100
www.ensaara.co.in

ID		Task Mo	Task Name	Start	Finish	% Complete
1			START	Sat 25-11-23	Sat 25-11-23	0%
2			Structure work & Blockwork	Fri 01-12-23	Fri 15-03-24	43%
3			External Painting	Fri 12-01-24	Mon 15-04-2	4%
4			Aluminium Windows	Thu 25-04-2	Sat 01-06-24	0%
5			Door frames	Thu 25-04-2	Mon 10-06-2	0%
6			Lobby & Passage tiles	Thu 25-04-2	Sat 15-06-24	0%
7			TILING work- flooring & Da	Fri 01-03-24	Thu 30-05-24	0%
8			Internal Cement Plaster	Wed 13-03-2	Mon 15-04-2	0%
9			Door Shutters	Tue 11-06-2	Mon 24-06-2	0%
10			Internal Painting	Thu 25-04-2	Sat 15-06-24	0%
11			External & Internal Plumbi	Thu 01-02-2	Sat 15-06-24	0%
12			UGWT	Thu 25-04-2	Fri 24-05-24	0%
13			MS Railing	Thu 25-04-2	Wed 26-06-2	0%
14			Water-proofing	Thu 25-04-2	Mon 17-06-2	0%
15			Electrical work	Thu 25-04-2	Sat 22-06-24	0%
16			CP & Sanitary Fixtures	Thu 25-04-2	Sat 22-06-24	0%
17			Stilt and Ground develop	Thu 25-04-2	Mon 10-06-2	0%
18			FINISH	Tue 25-06-2	Wed 26-06-2	0%

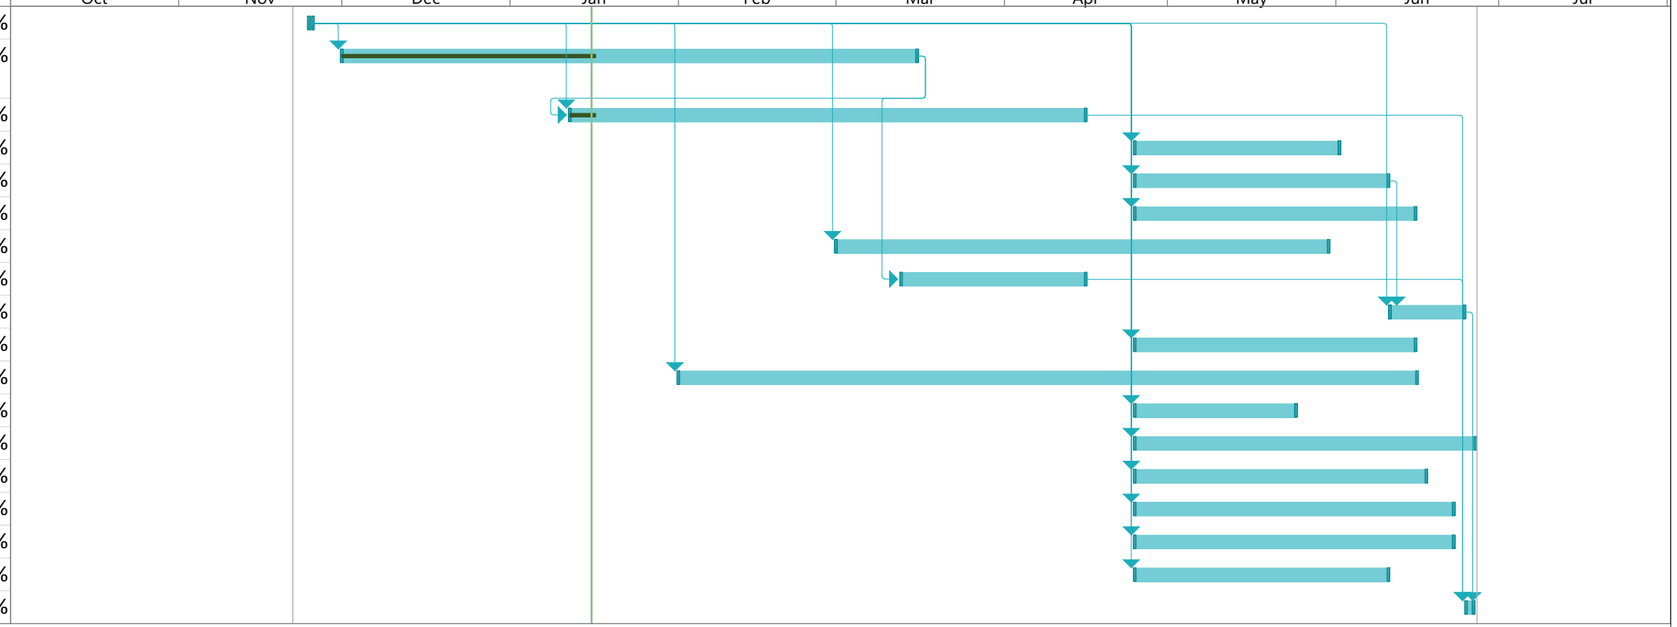

Project: Vista 3 C updated on 1
Date: Tue 16-01-24

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	
