FORM-2A

(MAHARERA ORDER NO 5 OF 2018)

ENGINEER'S CERTIFICATE FOR QUALITY ASSURANCE

(Site Supervisor's Certificate)

To,
Goel Ganga Infrastructure and Real Estate Pvt Ltd.
3rd Floor San Mahu Complex,
Bund Garden Road,
Opp Poona Club, Camp,
Pune -411001.

Quality Assurance Certificate

Certificate no- GS 3rd floor


Subject : Certificate for quality of materials used and quality of Construction and workmanship for the Work of "Glocal Square "
Project - GlocalSquare3RD Floor

Glocal Square -3rd Floor -Wing A,B, C and D
Situated at CTS Nos 3118, 3120, 3121 and 3124, BUTY MAHAL ,Khasra Nos. 315 P and 320 Ward No.3, Sitabuldi Nagpur.

Demarcated by its boundaries
East –Nala
West-Abhyankar road
North- 18 m wide Existing Sitabuldi Road
South- NMC School

Admeasuring 4463.28Sq.mts.area being developed by Goel Ganga Infrastructure and Real Estate Pvt Ltd

MAHARERA registration No –P50500025959

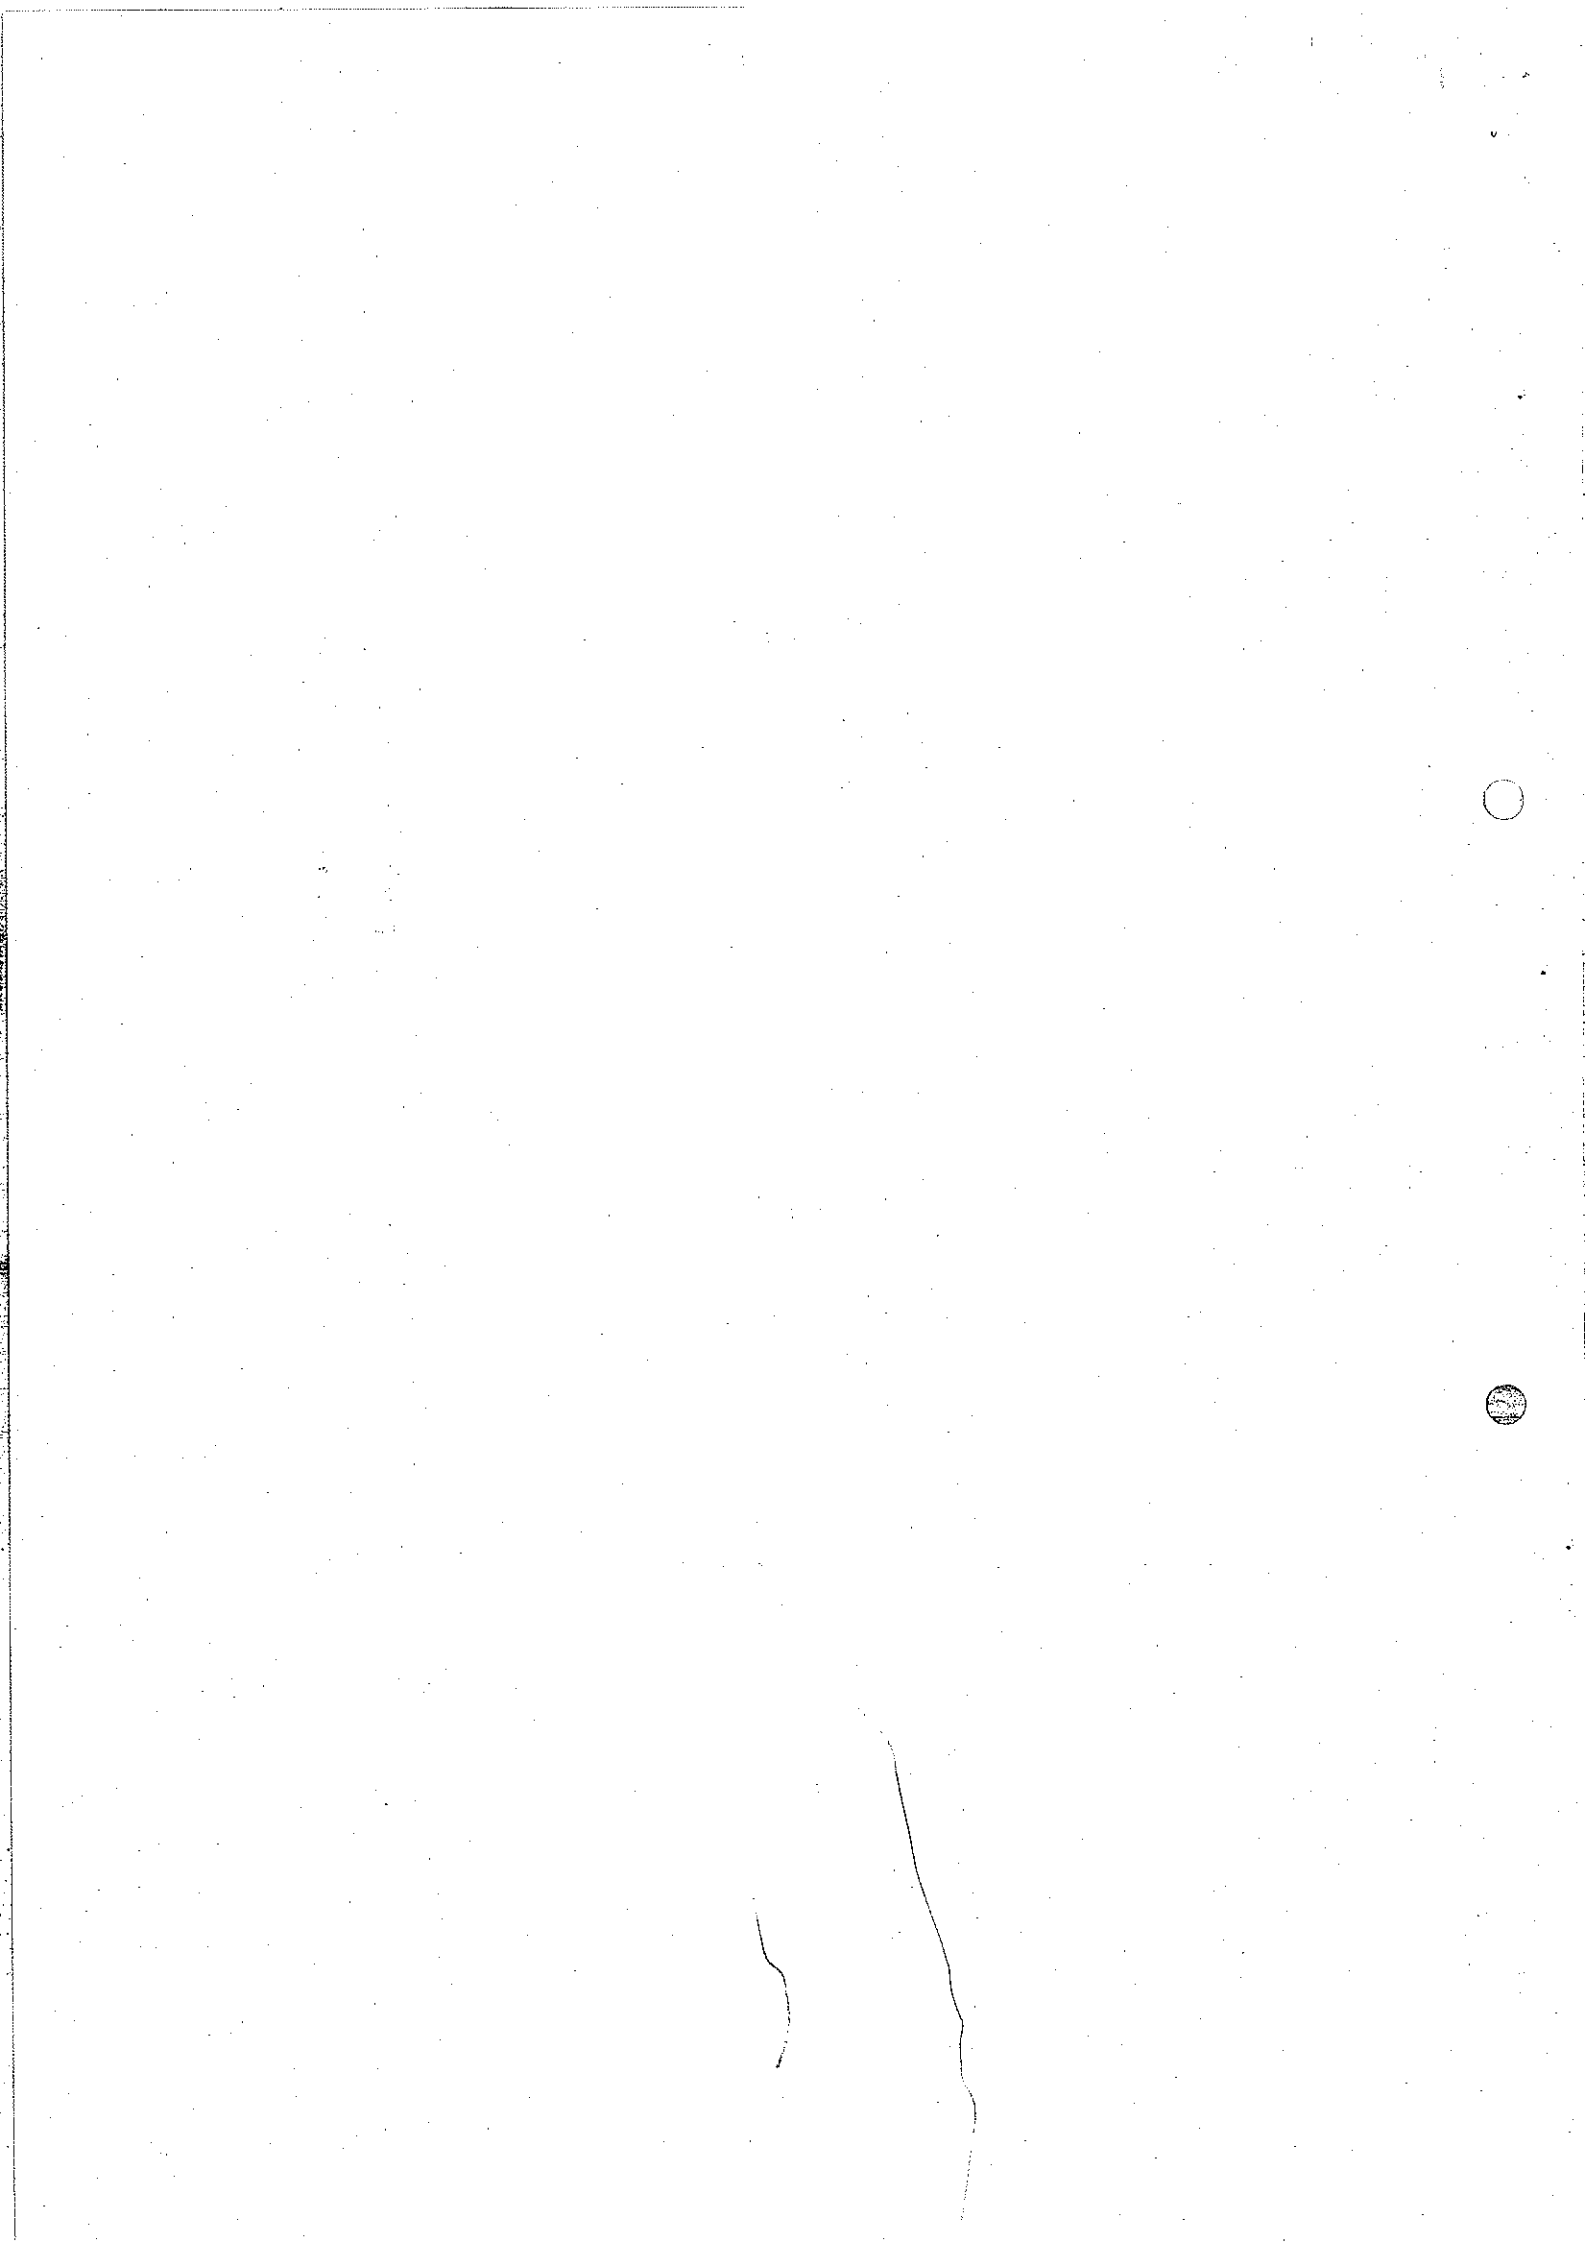

Sir,

I **Anand Shirsat** have undertaken an assignment of supervision of this real estate project for **Lower Ground Floor and Second Floor RCC and Finishing work.**

1.**My Responsibility: -**
To carry out the work in accordance with the development permission and as per the Approved plan and submit certificate of supervision of work and to carry out material Testing in-situ or in the authorized laboratory and to ensure quality of work and Workmanship as per prescribed specifications, and as per NBC and or other relevant Code of practice.

1. **Material Testing**
I have applied following mandatory checks on the basic materials, used in the construction.

i. Cement-
It has been tested for its fineness, soundness, setting time, compressive strength etc. as per IS code 3535:1986 or as per other relevant IS/BS/NBC code, or as per industry standards and its results are within the permissible limits.

ii. Coarse aggregate -
It has been tested, for deleterious materials, clay lumps, crushing value, impact value as per IS 243011986 or as per other relevant IS/BS/NBC code or as per industry standards and its results are within the permissible limits.

iii. Bricks/ blocks -
They have been tested for water absorption, crushing strength etc. as per IS 5454:1978 or as per other relevant IS/BS/NBC code or as per industry standards and its results are within permissible limits.

iv. Concrete / Ready-mix Concrete-
It has been tested for compressive strength for various periods as per IS 456:2000 and IS 1199 or as per other relevant IS/BS/NBC codes, as per industry standards and its results are within permissible limits.

v. Steel for concrete-
It has been tested as per IS 2062:2011 or as per other relevant IS/BS/NBC code or as per industry standards for tensile strength, elongation and gauge length etc. and its results are within permissible limits.

vi. Testing of Other materials -
Other materials like sand, crushed sand, floor tiles, fixtures and fittings, Pipes and sanitary fittings etc. (List out all items) used in this project conform to relevant IS/BS/NBC code or as per standards laid down by the industry for a Particular material.

2. Workmanship:-
I hereby certify that work has been carried out under our supervision. I Further certify that workmanship and quality is satisfactory and up to the mark andthe work has been acceptable within the permissible limits of deviations as per relevant code of practice.

3. Electrical Materials and workmanship: -

Works of all the electrical wiring/ connections / lift installation / other Electrical installations have been carried out under authorized /registered Electrical engineer and its .Records has been maintained. The materials used Conform to the relevant I.S/ B.S/ National Building codes or as per industry Standards.

4. Structural engineer: -

Promoters has engaged structural engineer **M/S .JW Consultants LLPSTR/W/10**.having office no.- cell no 20266449100

The structural design of buildings in this project has been done under his Supervision. He has checked the soil report before laying PCC for foundation in Consultation with soil consultant. The formwork and concrete mix design has been done as per IS 10262:2009 or as per other relevant codes as applicable. His periodic checks and certificates for STABILITY and SAFETY have been kept onRecord.

5. Preservation of records: -

Record of all test results of this project have been properly kept in the prescribed formats and will be preserved at least up to the defect liability period or for the period as required by any other provision of law

6. Please specify materials or any other item of work which were not conforming to the standard specifications and which were not rejected

1. NA

Yours Faithfully,

Name:-Anand Shirsat
